



# INSTALLATION CHECK LIST FOR NRG CODEMARK™ CERTIFICATION(Issue 3)

## INSTALLER

Name..... Company.....


Address.....

Phone..... Email.....

License No.....

## NRG GREENBOARD INSTALLATION CHECKLIST

- Installation has been completed in accordance with NRG Specifications Manual (Version 9, March 2017)
- Both Builder and Installer
  - are conversant with the method of Greenboard™ Installation and
  - have ready access to all relevant technical information related to Greenboard™ Installation
- NRG Greenboard™ is fixed in Accordance with fastener spacing's (table B, page 7). NRG Technical Manual e.g. 300mm centres vertically, 450mm centres horizontally
- Glue both horizontal and vertical. Greenboard™ sheet edges to each adjoining sheet using an approved construction glue or expanda foam
- Allow 3mm gap between Greenboard™ edge and openings for bead and sealing procedure (refer table 17.1.16, page 14) NRG Technical Manual (Version 9, March 2017).
- Expansion Joints are installed where NRG Greenboard™ meets other substrates
- Expansion Joints are installed horizontally maximum of 3 metre spacing and vertically maximum of 8 metre spacing (as per detail, DWR09 and DWR10 page 21)

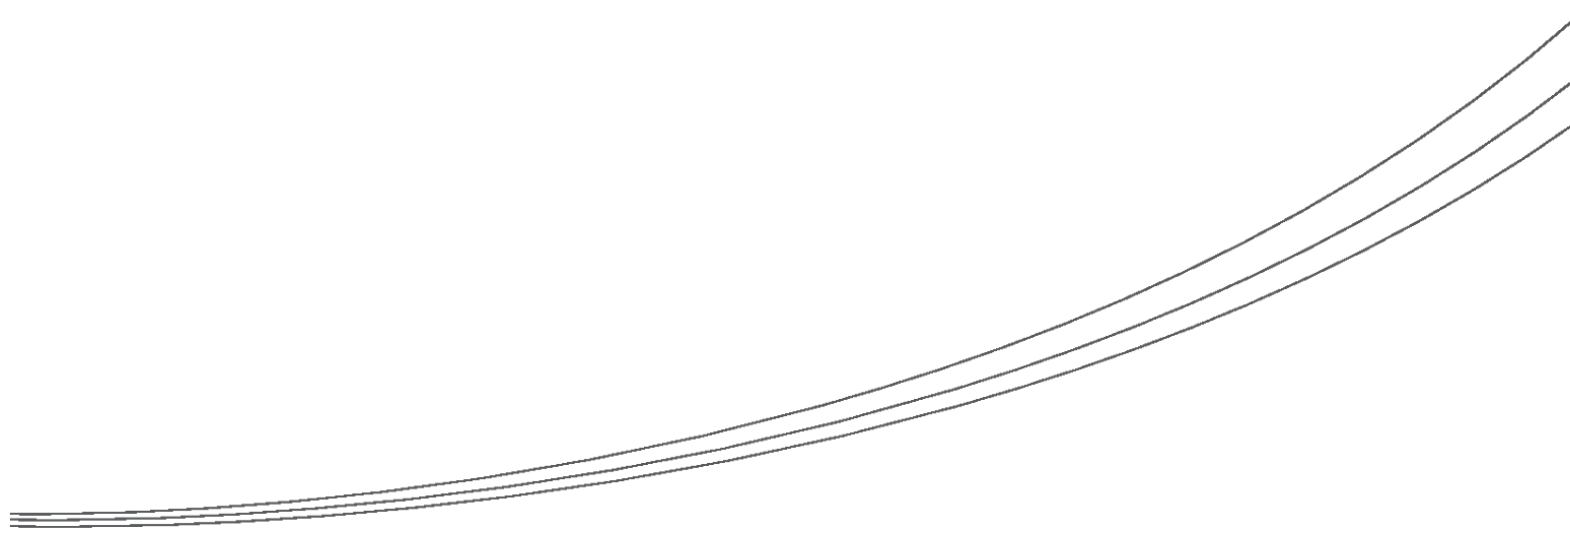

I the Installer have checked the checklist and have installed the NRG Greenboard™ Wall Cladding in accordance to NRG Greenboard™ Specification Manual (Version 9, March 2017).

Installer Signature.....

Date.....

p. 07 3382 7742 f. 07 3382 7741  
e. [HYPERLINK "mailto:sales@nrggreenboard.com"](mailto:sales@nrggreenboard.com)  
[sales@nrggreenboard.com](mailto:sales@nrggreenboard.com)  
w. [HYPERLINK "http://www.nrggreenboard.com"](http://www.nrggreenboard.com)  
[www.nrggreenboard.com](http://www.nrggreenboard.com)  
PO Box 2405, Burleigh MDC QLD 4220  
Factory 4, 32-38 Dover Drive, West Burleigh QLD 4220
